


# Frederick Road (MD 144) Interchange Reconstruction

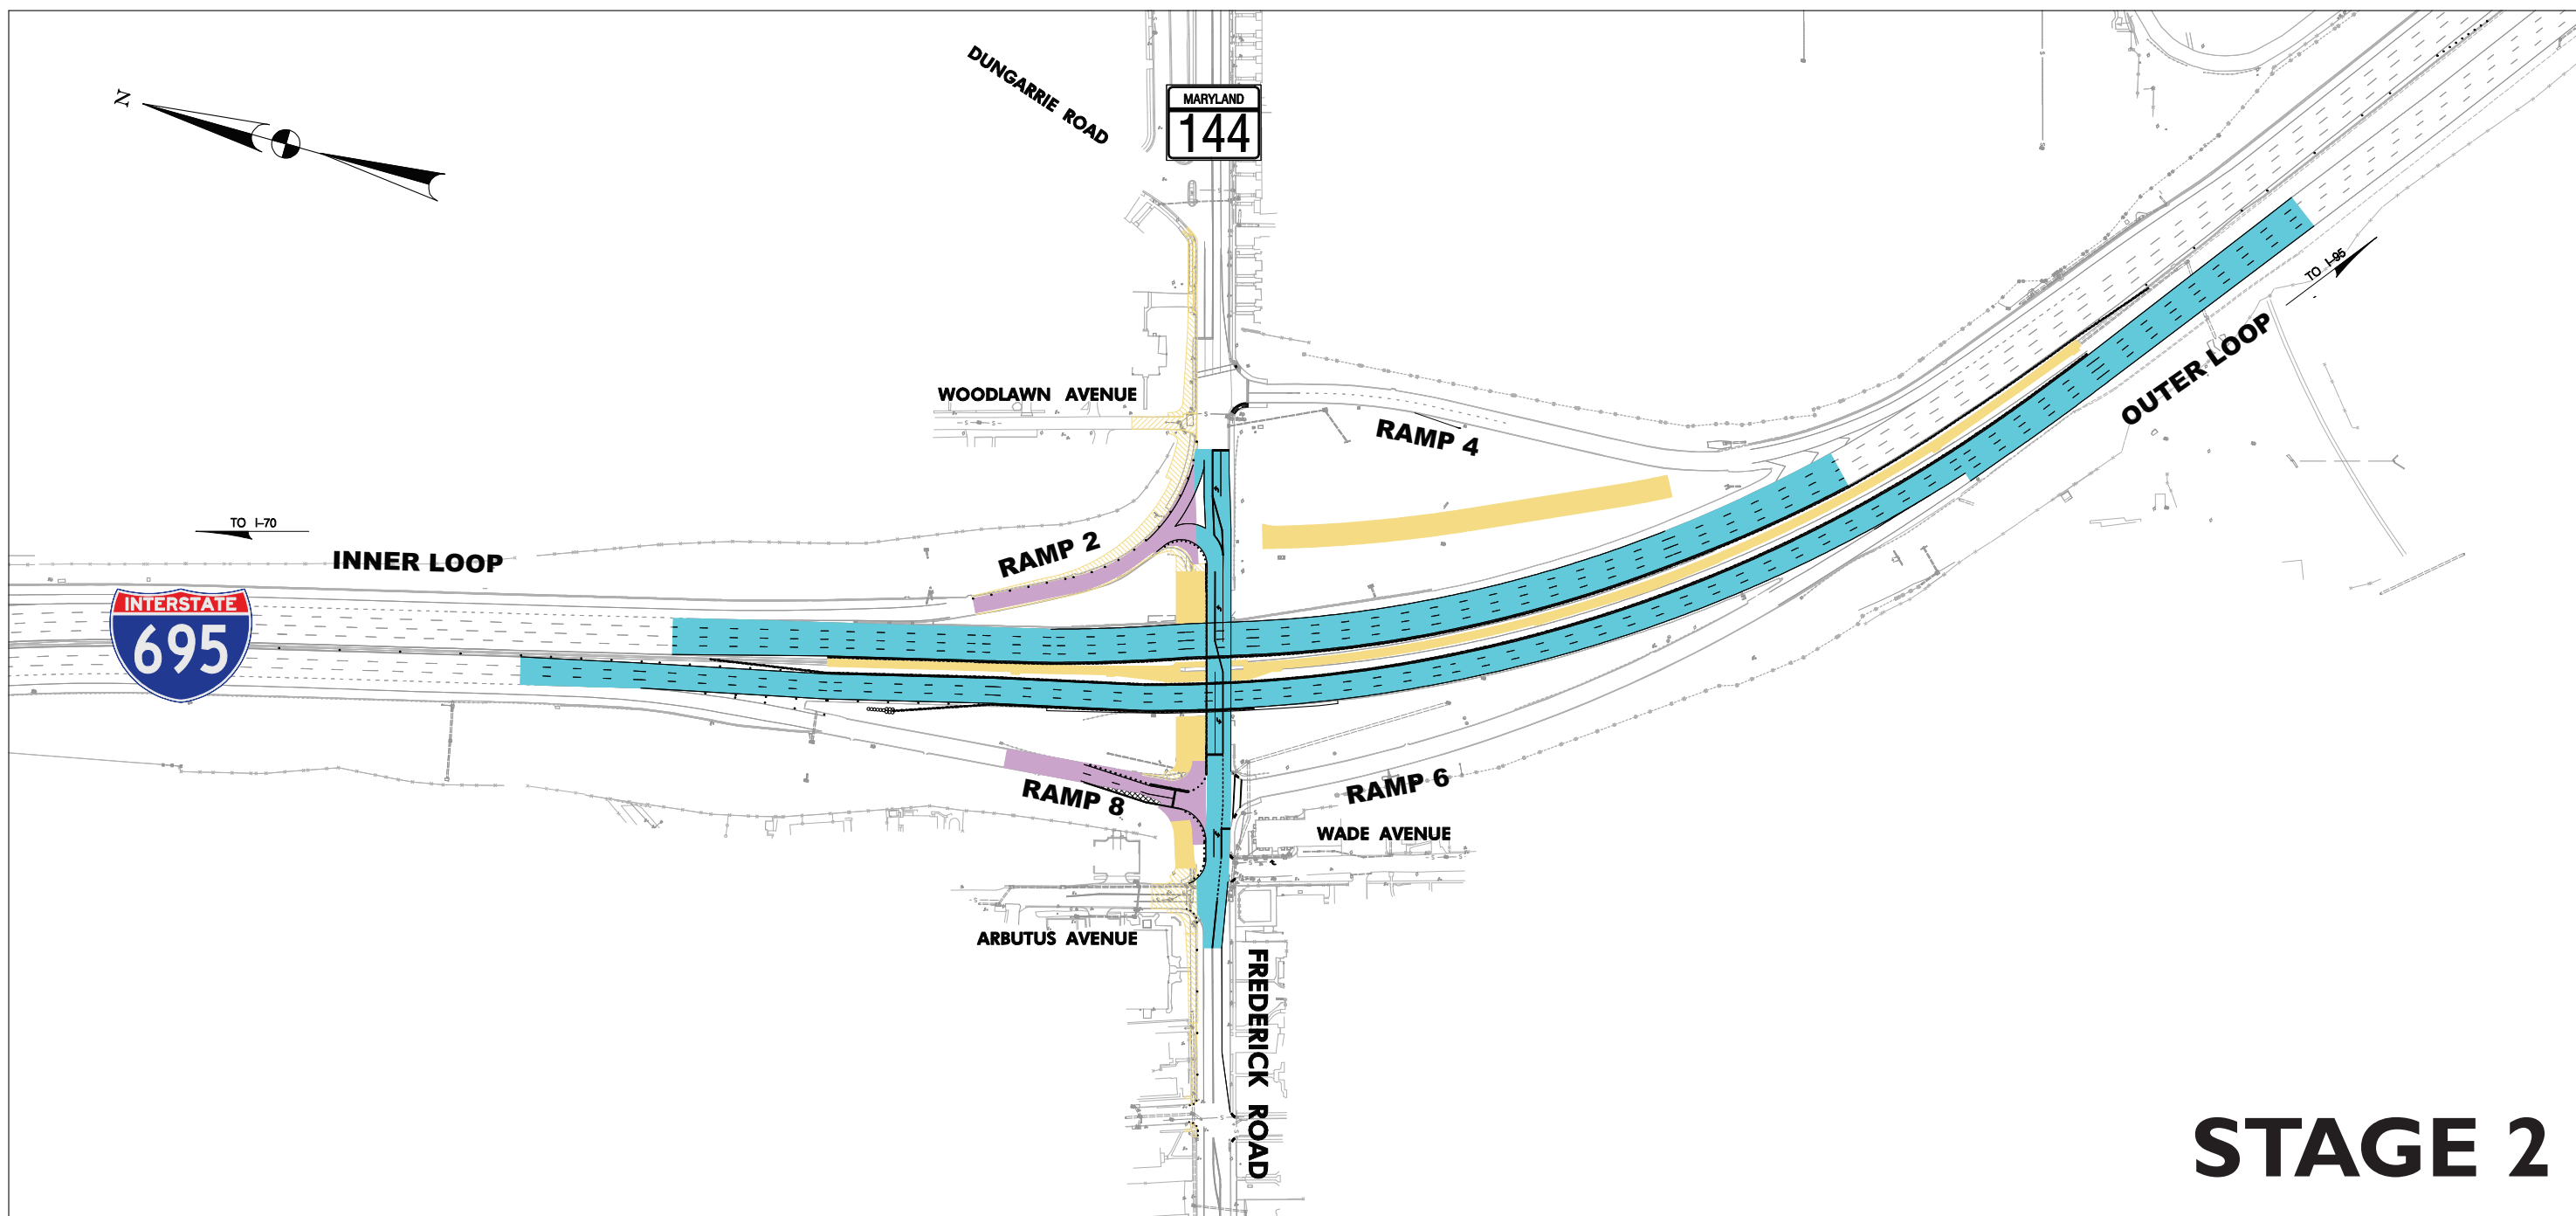

## STAGE 2

### Stage 1: Prepare Frederick Road (MD 144) and I-695 for Traffic Shifts (Not Shown)

- Remove existing island and portion of existing sidewalk on the bridge over I-695 using off-peak hour lane closures
- Construct temporary widening of the ramp from I-695 Outer Loop to Frederick Road (Ramp 8) and widen I-695 Outer Loop in the vicinity of the bridge
- Begin construction of realigned ramp from I-695 Inner Loop to Frederick Road (Ramp 4)

### Stage 2: Construct North Side of Frederick Road (MD 144)

- Shift I-695 travel lanes to the outside of the Inner Loop and Outer Loop roadways
- Shift Frederick Road travel lanes to the south side of the roadway
- Construct widening of the north side of Frederick Road, including demolition and reconstruction of the north side of the bridge
- Construct temporary traffic signal at the intersection of Wilkens Avenue (MD 372) with Kenwood Avenue (Not Shown)

- Reconstruct the ramp from Frederick Road to I-695 Inner Loop (Ramp 2). Ramp reconstruction is to be performed under overnight ramp closures. During the closures, ramp traffic will be detoured onto I-695 Outer Loop to Wilkens Avenue
- Continue construction of realigned ramp from I-695 Inner Loop to Frederick Road (Ramp 4)
- Begin construction of the new median barrier along I-695 within the project limits
- At the end of this construction stage, the ramp from I-695 Outer Loop to Frederick Road (Ramp 8) is to be reconstructed under a multiple week ramp closure. During the closure, ramp traffic will be detoured to Wilkens Avenue (MD 372)

